

Mt. Diablo Unified School District 2010 Measure C Facilities Improvement Program

Report to the Board of Education


September 24, 2014



- Accelerated Schedule
- Project Status
- Financials
- Measure "C" Project Highlights



2010 Measure C Accelerated Program Schedule

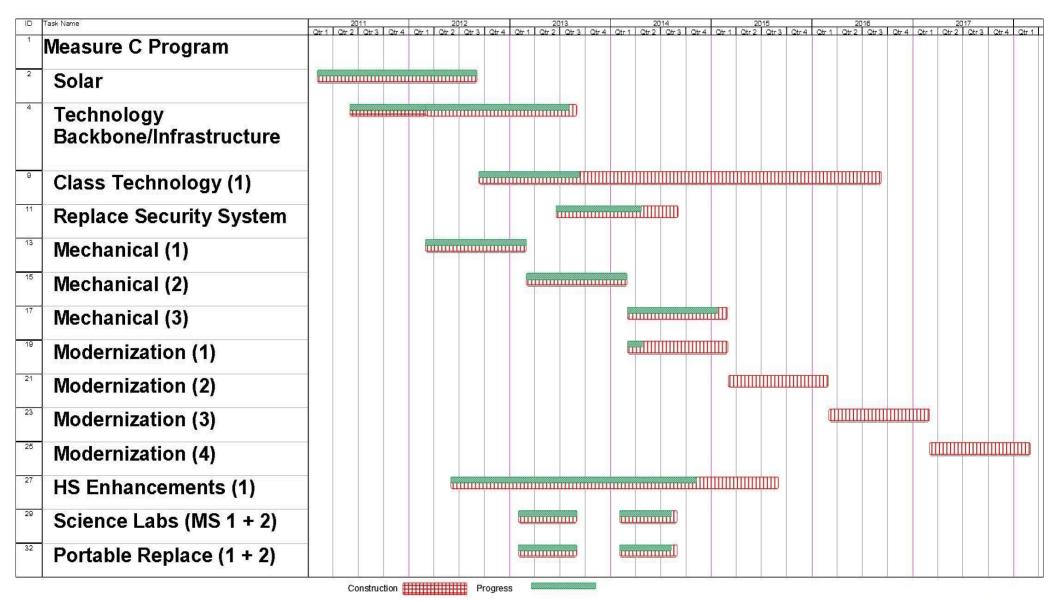





Project Status


- Solar Complete
- Infrastructure Improvements ~ 99% Complete
- HVAC (Classrooms/Administration) ~99% Complete
- Technology Classroom Improvements
 - Phase I Technology Labs ~ 98% Complete
 - Phase II Classroom Enhancement Planning
- Portable Replacement ~ 97% Complete
- MS Science Buildings Complete
- HS Enhancement Program ~ 51% Complete
- Modernization <10% Complete
- Security System Replacement ~ 75% Complete

Financials: 'Bid to Budget'

Project	Program Budget	Working Budget	Projected Commitment thru 7/31/2014
Solar	\$111,876,297	\$92,419,506	\$78,346,331
HVAC Group 1, 2 & 3	\$46,171,979	\$61,137,564	\$63,726,305
Portable			
Replacement,			
General Science, HS			
Enhancements	\$97,234,875	\$98,962,757	\$72,992,445
Technology	\$12,678,822	\$10,495,872	\$9,191,450
Modernization	\$65,654,502	\$55,436,659	\$3,163,744
Security	\$13,393,111	\$11,469,198	\$9,671,095
Total	\$347,009,586	\$329,921,556	\$237,091,370

^{*}Note: With the exception of HVAC all H.S. Enhancement, Portable Replacement, Middle School Science and Technology Bids/Procurements Awarded and Tracking Under Working Budgets

Financials: Cash Flow

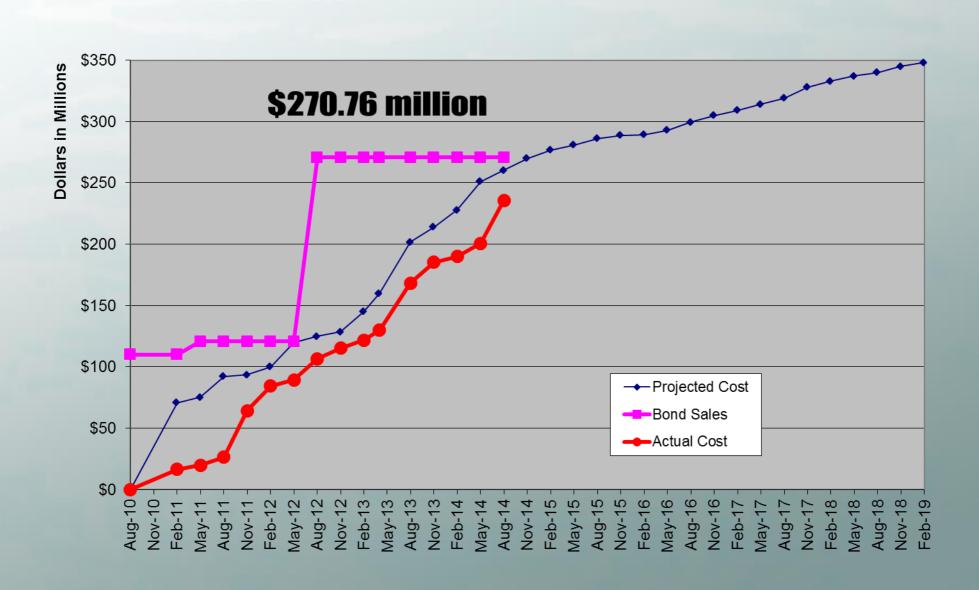

A STATE OF THE PARTY OF THE PAR

Measure C

SUMMER HIGHLIGHTS

- •~23,000 square feet of new classrooms
- •~282,077 square feet of space conditioned (1,118 tons)

SPRING/SUMMER 2015

- Stadium Improvement Projects (2)
- Security (all sites)
- Aquatics/Sports Med/Restroom Complex(1)
- Auxiliary "Mini" Gym (1)
- Technology Classroom Enhancements (15)
- Site Modernization Projects (11)

